



AWH Silver Line Regional Rail Project Construction Activity (CA) Notification

Construction Activity (CA) Details

Notification Date: Monday, February 20, 2023

Construction Activity Start Date: Friday, February 24, 2023

Construction Activity Work Time: 1. 3-Day Full Closure

Contractor Information:

Contractor: Archer Western Herzog (AWH)

Contractor Contact Name: Marvin Jackson, AWH PI/CR Manager

Construction Activity Location: Custer Parkway and the SLRR Guideway - 3-day full Closure


Address (If Applicable): N.A.

City, State Zip: Richardson, Texas

Scope of Construction Activity:

AWH and subcontractors ("crews") shall implement a 3-day full closure at Custer Parkway on Friday, February 24, 2023 for the installation of DART Silver Line Regional Rail tracks. The work is projected to be completed on Monday, February 27, 2023. Following the 3-day full closure, Crews to install Phase 2 switch to southbound lane closure. (1 southbound lane will be closed and 2 northbound lanes will remain open)

Note: This CA is a supplement to CA0122, Custer Pkwy Phased Lane Closures.

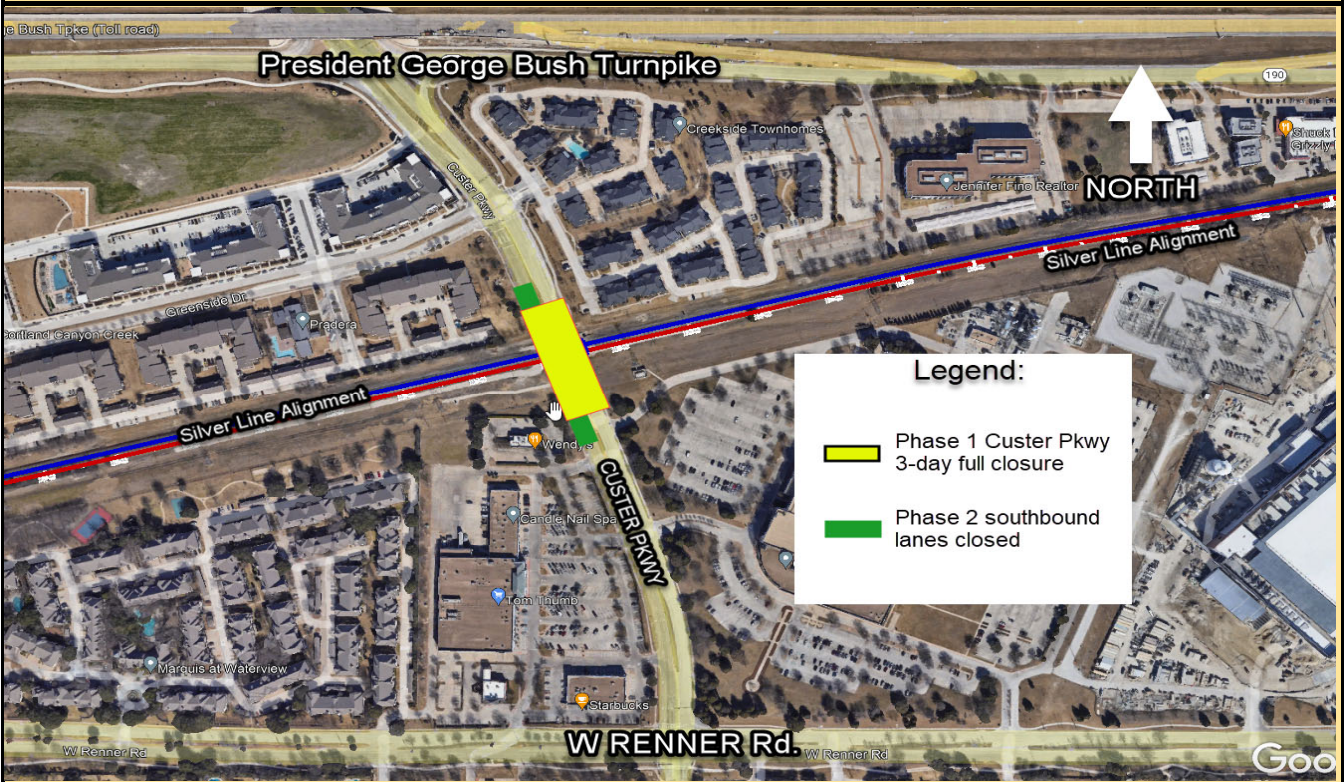



AWH Silver Line Regional Rail Project Construction Activity (CA) Notification

Construction Activity (CA) Details

The steps to 3-day full closure are as follows:

Step 1 - Crews to ensure proper 3-day full closure traffic control devices and video message boards are activated

Step 2 - Friday, February 24, 2023 at 9A, Crews to secure the 3-day work limits for pedestrians, vehicular traveling public, and workforce

Step 3 - Crews to perform rail installation across Custer Pkwy

Step 4 - Monday, February 27, 2023 once the 3-day closure is complete, Crews to install Pase 2 to complete Custer Pkwy work from CA0122.

Step 4 - Once complete, Crews to clean-up and demobilize from the area

Note: AWH Public Information/Community Relations ("PI/CR") team will notify residentially adjacent property owners to this scope of work of this upcoming activity. Street sweeping and flagging access will be maintained throughout construction activities.

Permits Submitted:

1. Permit Pending

AWH Contractor Contacts:

AWH Safety Mgr. Bill Abbott, (817) 538-0081

AWH QC Mgr. Jim Grady, (817) 823-8846

AWH CA Mgr. Marvin Jackson, (214) 585-7308

Construction Hotline 972.833.2856

Report Prepared by: Marvin Jackson, AWH

Title: CBRR CR&PI Manager

Report Title: 20230217 - CA0149 - Custer_Crossing_-_3-Day_Full_Closures_-_Richardson
